




TEXAS DEPARTMENT OF TRANSPORTATION



WEBB COUNTY/ CITY OF LAREDO PROJECT STATUS

Roberto Rodriguez, P.E
Laredo District

January 22, 2019

Projects Under Construction


Under Construction (Carlos G. Rodriguez, P.E.):

- *SL20 Over KCS RR Grade Separation:*
 - *Work is 87% Completed. Anticipated Termination Date: Early Summer 2019*
- *US 59 Over IH 35 Overpass:*
 - *Work is 55% Completed. Anticipated Termination Date: Winter 2019*
- *SH 359 From City of Laredo to Duval County:*
 - *Work To start in Late January 2019. Anticipated Termination Date: Summer 2020*
- *US 83 From Dimmit County Line to 3.4 MI S of SH 44:*
 - *Work To start in Spring 2019. Anticipated Termination Date: Summer 2022*

Major Mobility Projects (Funded):

US 59 (Future IH-69W):


- *5 Overpasses (Interchanges):*
 - *Shiloh- \$ 21.5 Mill, Letting February 2022*
 - *Del Mar- \$ 24.1 Mill, Letting February 2022*
 - *University- \$ 16.9 Mill, Letting February 2022*
 - *Jacaman- \$ 19.7 Mill, Letting August 2021*
 - *Airport- \$ 14.8 Mill, Letting August 2024*

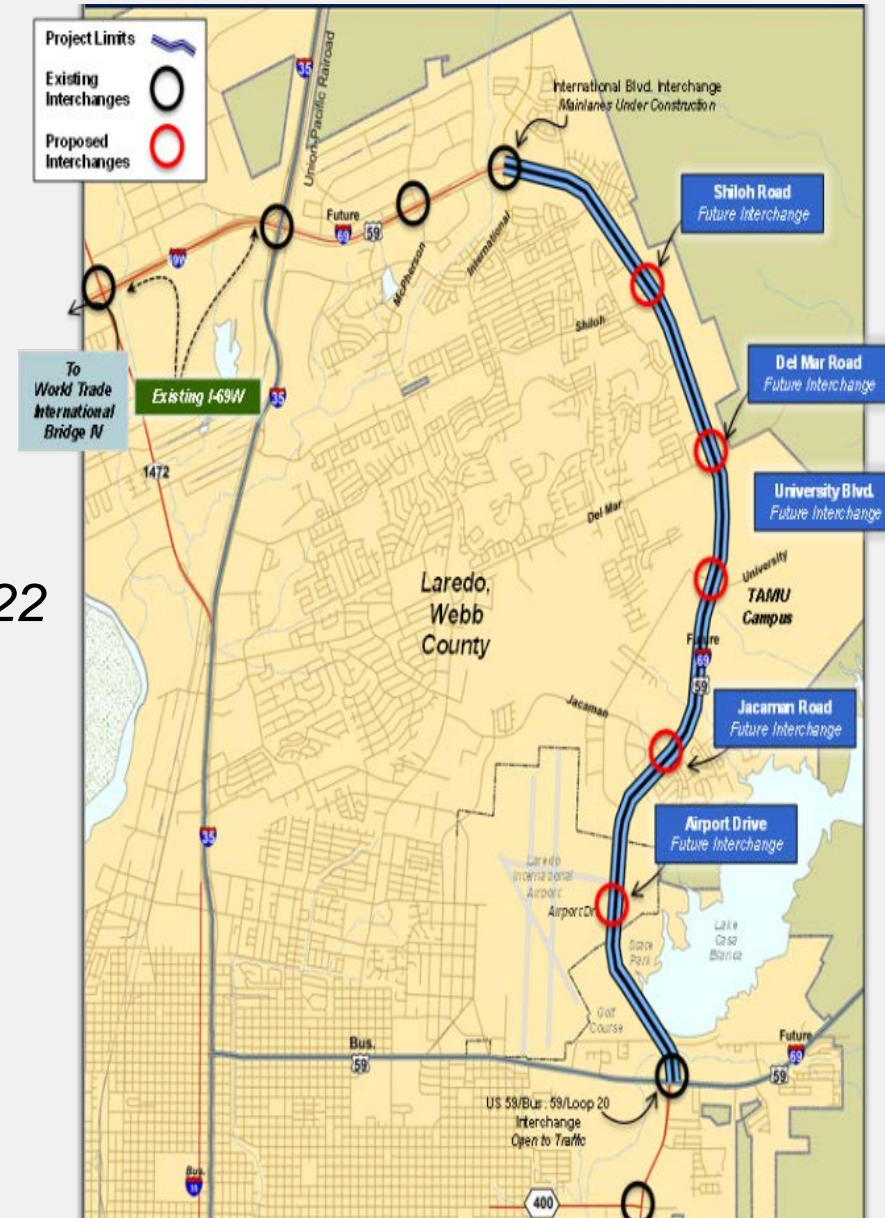

Major Mobility Projects (Funded):

IH 69:


- Widening IH 69 to 6 Lanes from World Trade GSA to IH 35. FM 1472 Improvements \$ 18.34, Letting August 2020

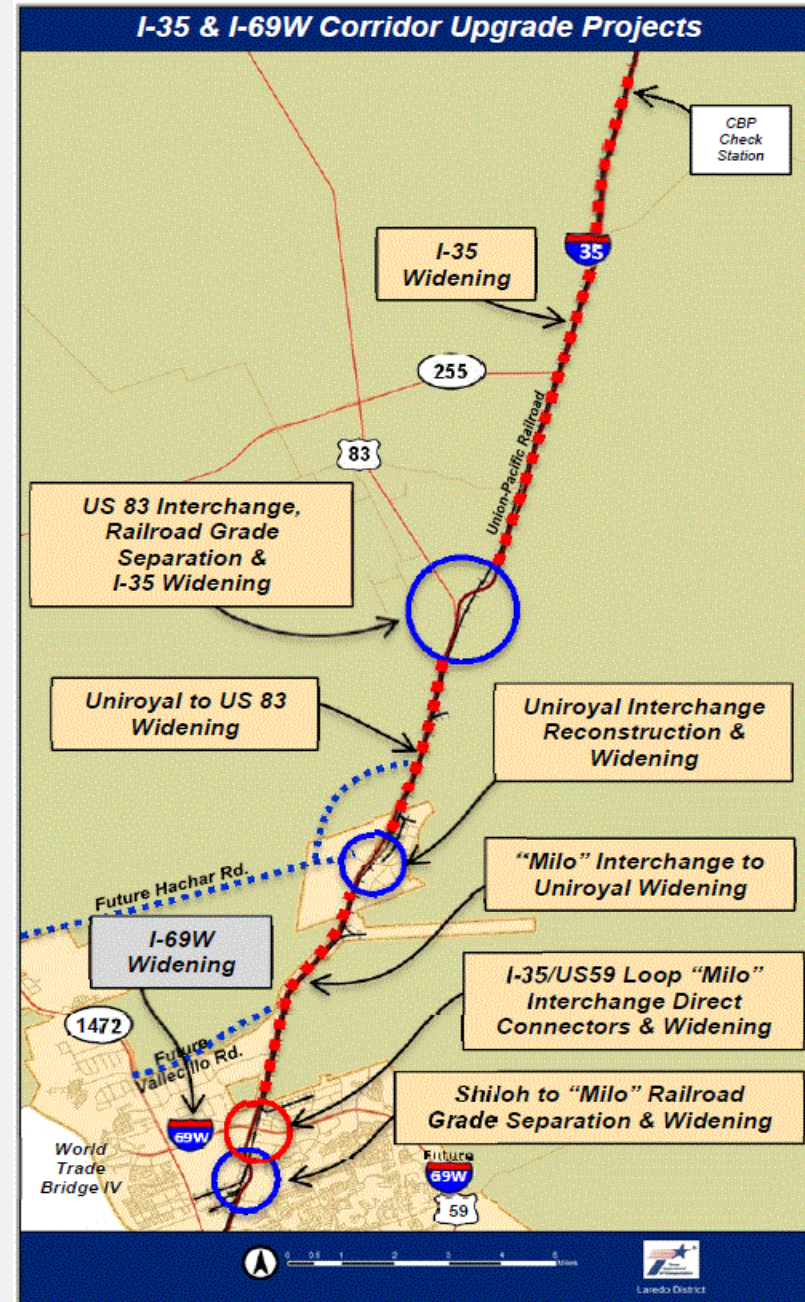

Major Mobility Projects (Funded):

IH 35:


- *Bridge Replacement and Widening to 6 lanes at UPRR- North of Shiloh - \$ 54.0 Mill, Letting December 2019*
- *Direct Connector # 5, West on US 59 to IH 35 South \$ 30.0 Mill, Letting December 2019*
- *IH 35 widening to 6 lanes at US 59 Interchange, \$ 5.0 Mill, Letting December 2019*
- *Bridge Replacement and Widening to 6 lanes at Uniroyal Interchange - \$ 65.0 Mill, Letting September 2021*
- *Bridge Replacement and Widening to 6 lanes at UPRR- Mile Marker 18 - \$ 75.0 Mill, Letting September 2021*

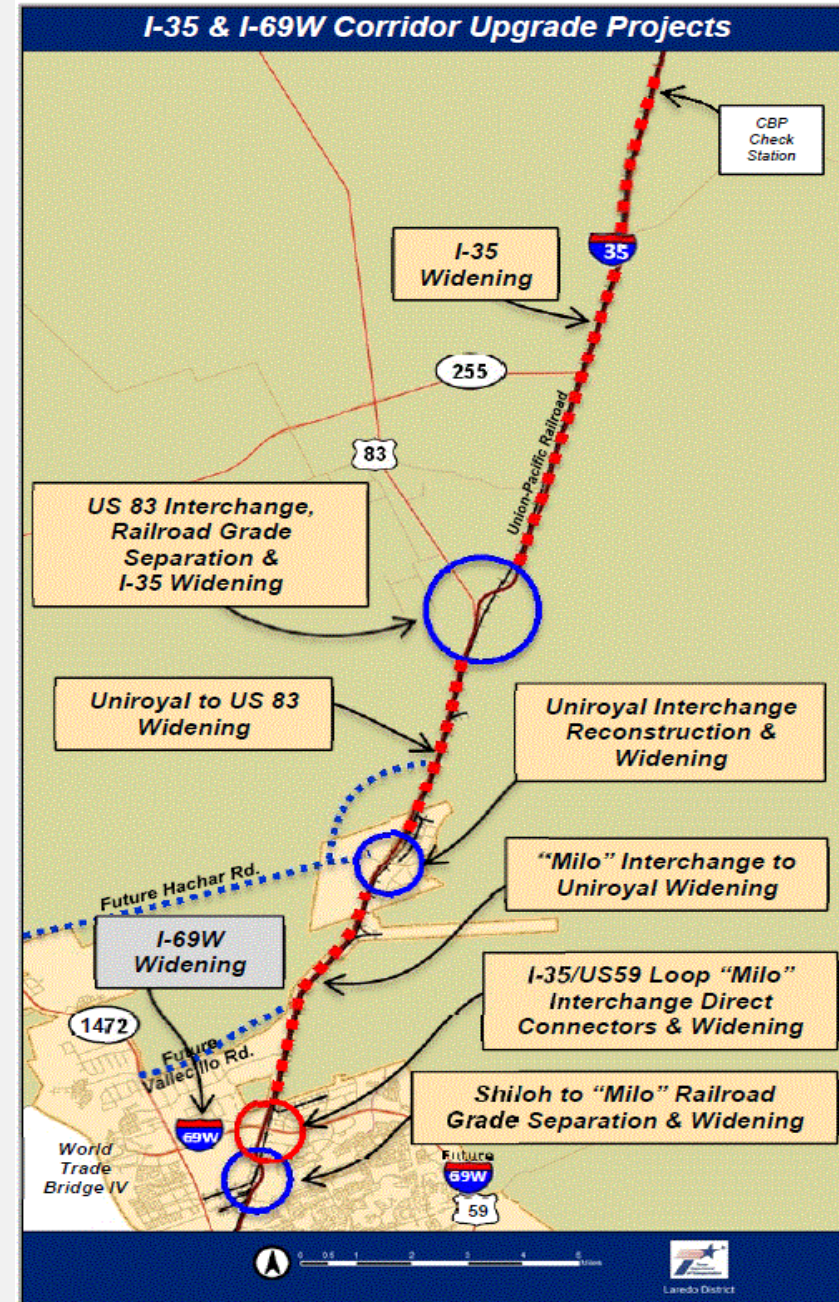

Major Mobility Projects (Not Funded/ Under Development):

Not Funded/ Under Development:


- *IH 35/ US 59 Construct Direct Connectors (4 Remaining) Approx \$ 90 Mill*
- *IH 35 at Carriers and Unnamed Overpass, Widening of bridges Approx \$ 45 Mill*
- *IH 35 from Mile Marker 20 to Mile Marker 30 (1 Mi North of Border Patrol Inspection), Widening to 6 lanes Approx \$ 70 Mill*
- *US 59 (Future IH69W) from BU59 to International Blvd, Upgrade to Freeway (Main Lanes and Frontage Rds) Approx \$ 107 Mill*

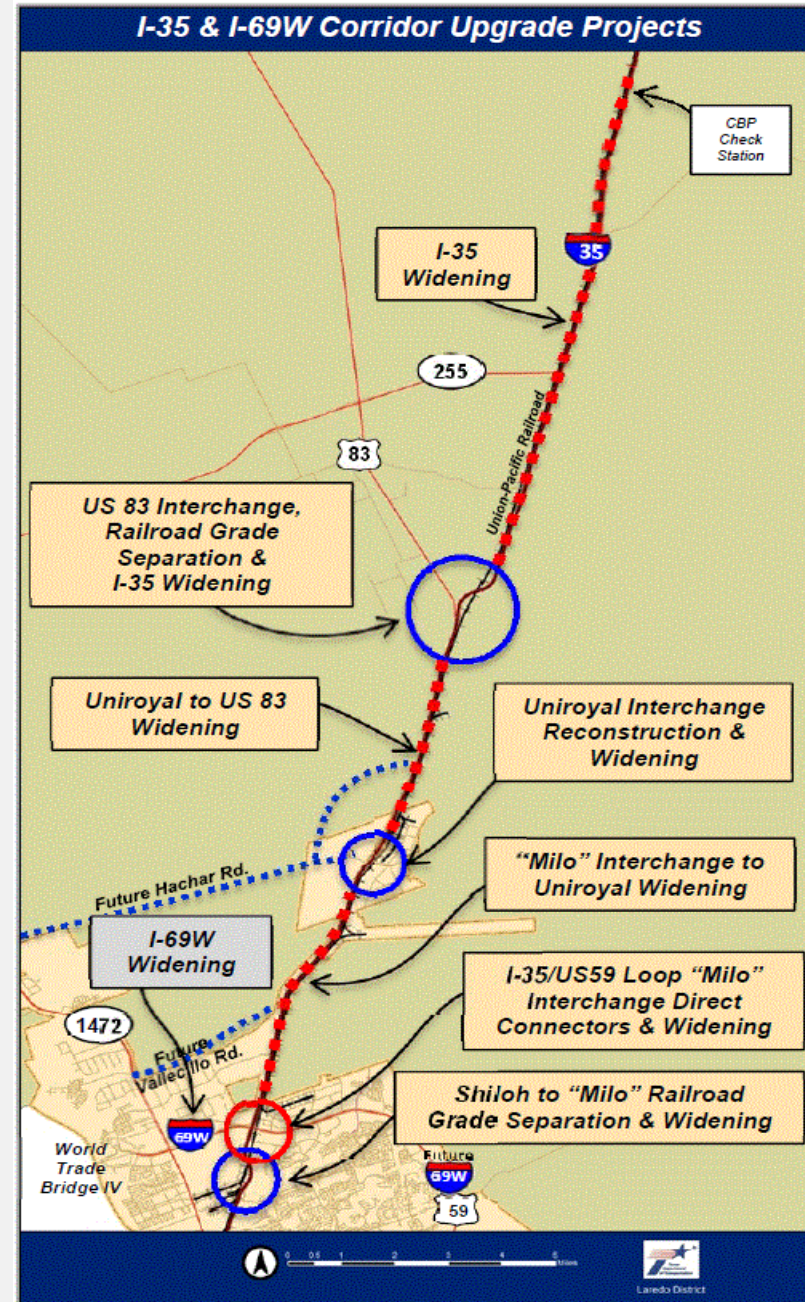

Major Mobility Projects (Not Funded/ Under Development):

Not Funded/ Under Development :

- *SH 359 Widening (Undivided / Divided Highway)
4.0 Miles East of SL 20 to 5 Miles East Approx \$
25 Mill*
- *US 83 Widening to 4 Lanes Divided From IH 35
to SH 255. Approx \$ 55 Mill*
- *FM 3338 Widening to 5 lanes From FM 1472 to
SH 255. Approx \$ 45 Mill*
- *Under Study – Laredo Outer Loop Approx \$ 480
Mill*

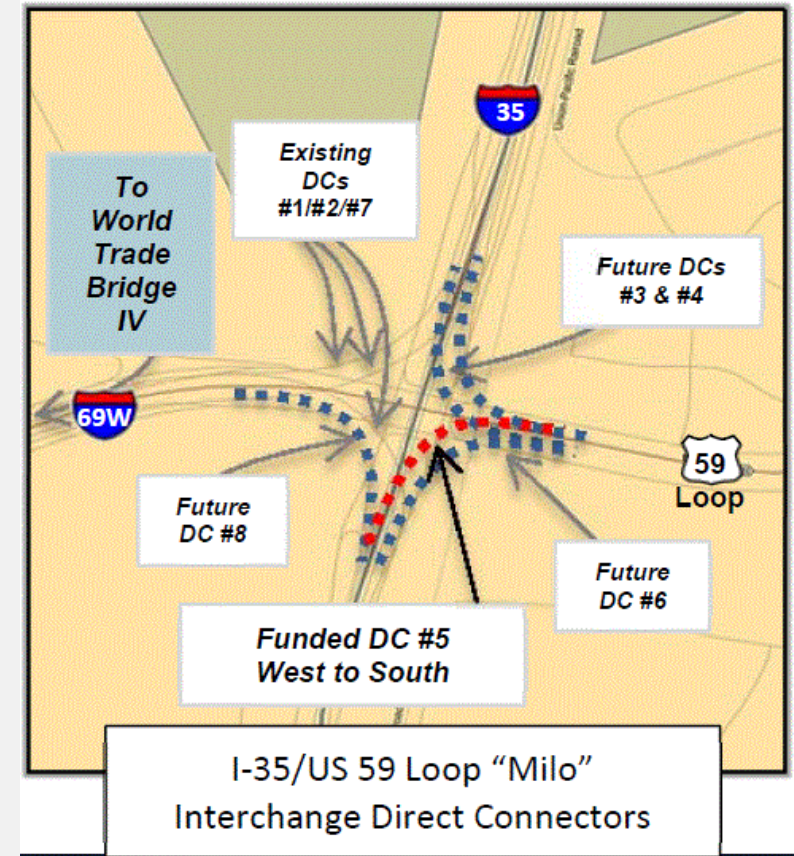

Laredo District/ Webb County/ Laredo MPO):

Projects Funded To Let Up to FY 2023:


- *Mobility: \$ 345 Mill*
- *Preventive Maintenance, Rehabilitation, and Safety: (up to FY 22) \$ 247 Mill*

Projects Under Design Up to PS&E (Ready to Let)

- *Mobility: \$ 437 Mill*

Projects Under Study

- *Laredo Outer Loop Approx \$ 480 Mill*

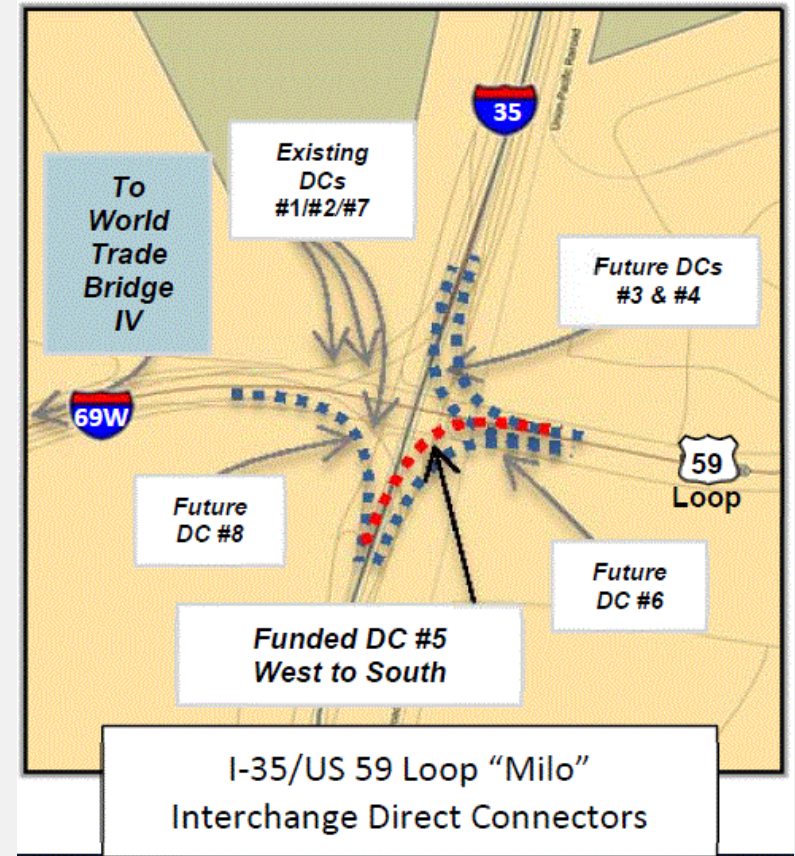

Questions?


David Salazar, P.E

TxDOT – Laredo District Engineer

1817 Bob Bullock Loop, Laredo TX 78043

E-mail: David.Salazar@txdot.gov

Phone: (956) 712-7400

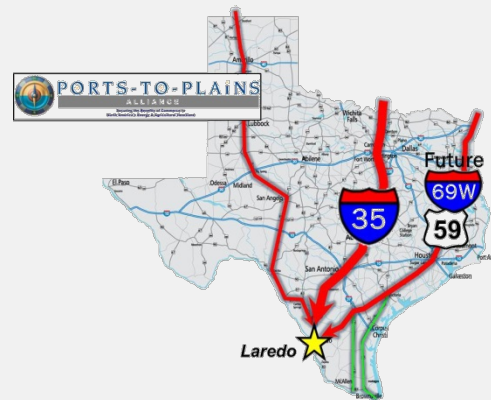

**Three Major Freight Corridors:
One Major Destination**

